



Docklands
Light Railway



Communications Session

- Progress of the Emirates Line Project
- Critical Issues
- Operation
- Questions

South Station Start on Site June 2011



South Station - December 2011



Communications Session

South Station - December

South Station Doppelmayr Bull Wheel mechanical assembly works complete,
Cabin store frame 100% complete.



Communications Session

South Station – Complete May 2012



Communications Session

South Tower – Mobilise barge August 2011



Communications Session

South Tower – Mobilise barge August 2011



Communications Session

Work Commenced 27th June 2011

North Station Piling Complete September 2011



Communications Session

North Station Concrete Works Complete 20th December 2011



Communications Session



Communications Session

North and North Intermediate Steel Towers

NIT - Erection commenced on Tues 6th December with phase 1 being successfully erected with the target of the tower being fully complete before Christmas achieved.

North Tower - The first 300mm of the pile cap has been poured, wrapping of the bolts has commenced and the final pour for the pile cap is planned for the 11th January 2011.



[N.I. Tower Erection Quick Time](#)

Progress Narrative December 2011




Critical Issues for 2012


- South Tower Base
Complete pile cap 13th
Feb 2012
- South Tower
manufacture and
erection by 9th March
2012
- Cable Pull, 3rd to the
10th March 2012



Cable Pull – 3rd March – 10th March 2012

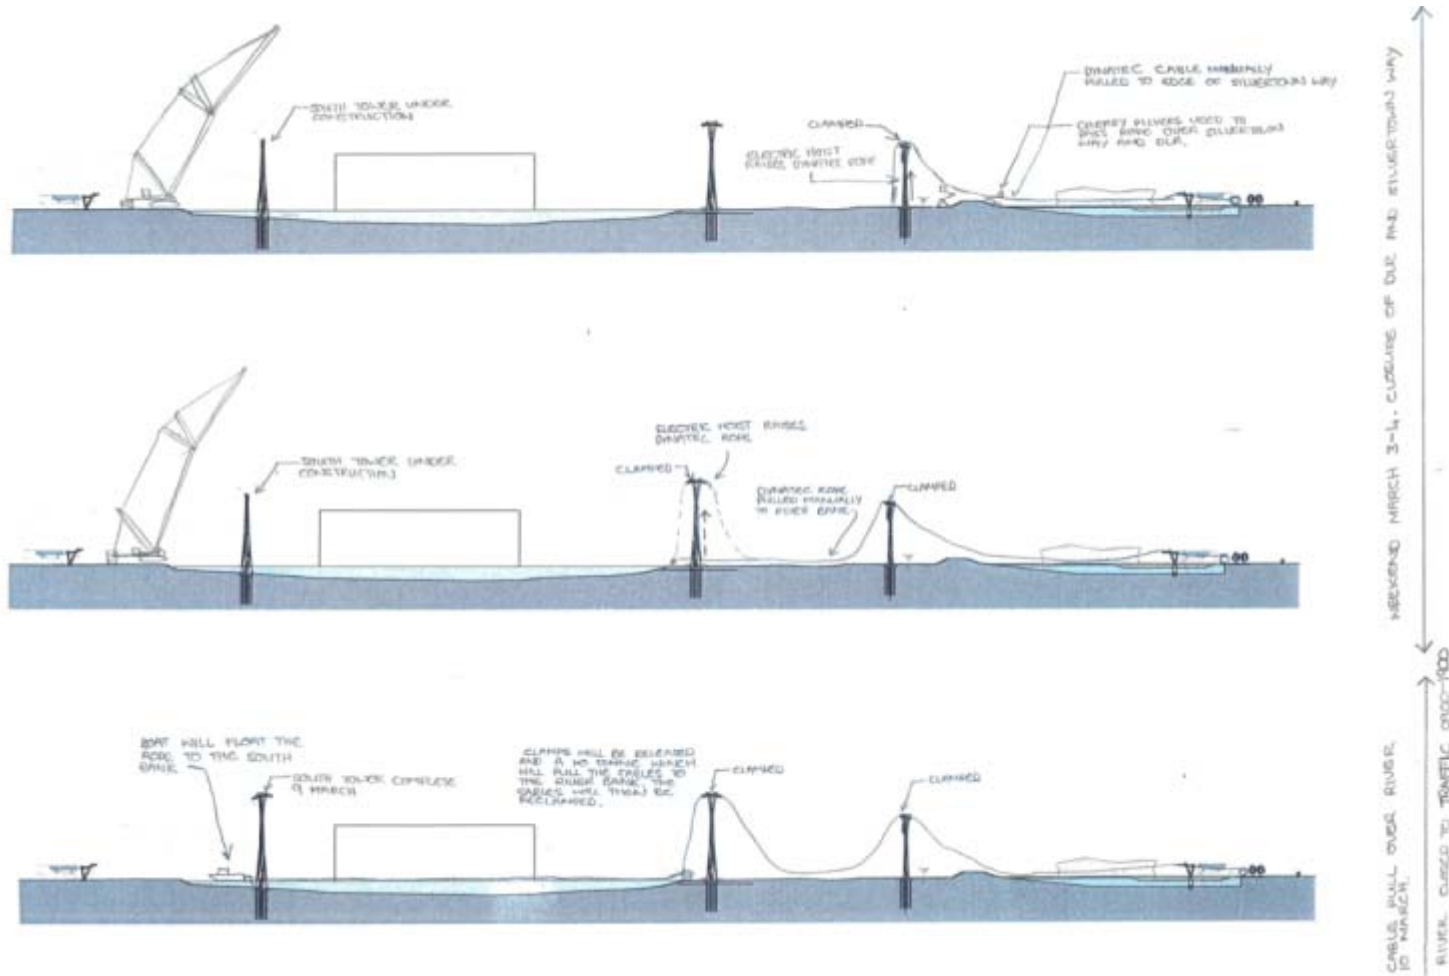

Cable Pull – 3rd March – 10th March 2012

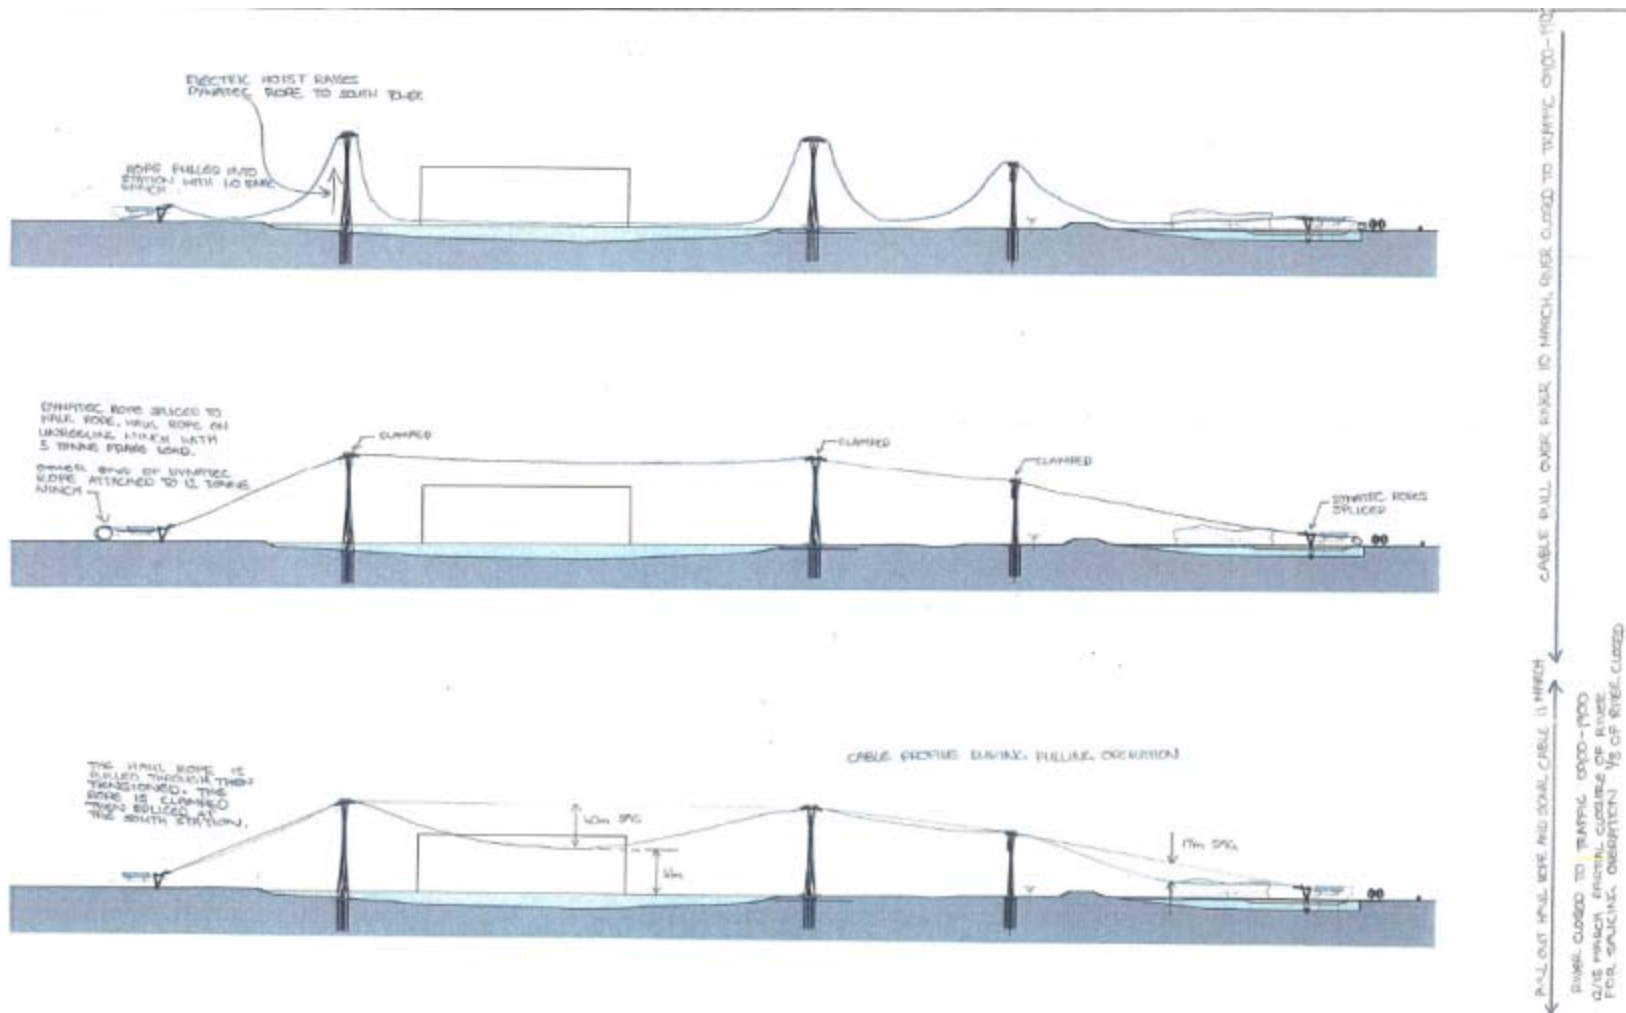

How would it work?

Operation

- Small gondolas, up to 10 passengers
- Continually circulating cable, gondolas spaced to a minimum of 15 seconds apart
- Little or no wait time
- Maximum capacity of up to 2,500 each way per hour – substantial queuing not expected under normal operation

Users

- Mixture of public transport users (i.e. using the cable car as a local transport link) and tourist/visitor trips
- Estimated circa 1 million in 2013 rising to 1.5 million by 2026

Fares / payment

- Payment by Oyster card – similar to Thames Clippers arrangement



Planning Application was submitted 28th October 2010
Unanimously approved January 2011
Referred to Mayor April 2011
Mace in Contract on 15th April 2011
Opening planned for Summer 2012



Communications Session

Questions
